

UTILITY SERVICE
CUSTOMER SERVICE
535 COURTNEY HODGES BLVD
P.O. BOX 1350
PERRY, GA 31069
TEL 800-223-3695
FAX 478-987-2529
WWW.UTILITYSERVICE.COM



City Of Fairfax Washout Inspection Report

Tank Information for Customer #5533

- **Tank Name:** University Tank
- **Tank Size/Style:** 4,000,000 Standpipe
- **Tank Location:** University Campus
- **Project Number:** 110259
- **Service Request:** 359279
- **Inspection Date:** December 28, 2012
- **Report Author:** Chris Palmer
- **Inspected By:** Timothy Clark

Customer Contact Information

- **Administrative:** Lauren S Sufleta
- **Job:** Rick Thoesen
- **Address:** 10455 Armstrong Street
Fairfax, VA 22030
- **Telephone:** 703-359-2495



Summary


A visual inspection was performed on the exterior condition. The tank is in good condition. The interior coating was not inspected but will be in 2014 when the interior will be cleaned, inspected and disinfected.

Coating Type & Conditions


- Interior Coating Condition: The interior coatings were not inspected but will be at the next interior inspection, cleaning and disinfection.
- Exterior Coating Condition: Exterior coating is in good condition.
- Dry Interior Condition : The interior coatings were not inspected but will be at the next interior inspection, cleaning and disinfection.



Exterior

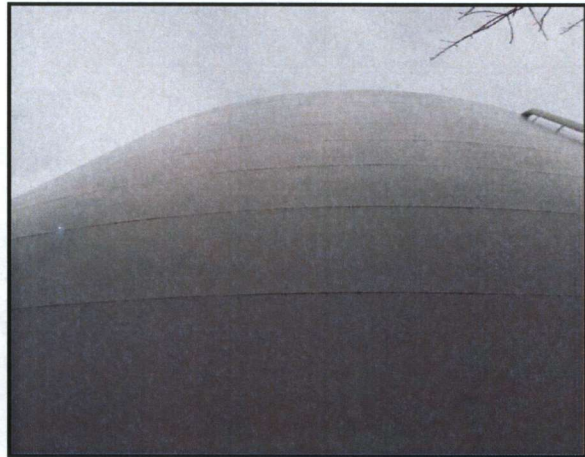


Exterior

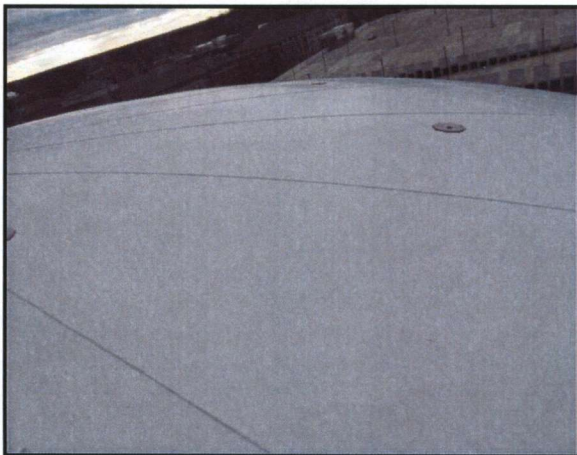

Exterior

Safety & Sanitation


- Safety Climbing Devices: Ladders are equipped with secured safety climb devices.
- Access Hatch1: Good
- Access-Hatch2: Good
- Vent Screen: Vent screen was replaced at the inspection.
- Evidence Of Foreign Matter: The interior was not inspected.
- Sediments: The interior was not inspected.

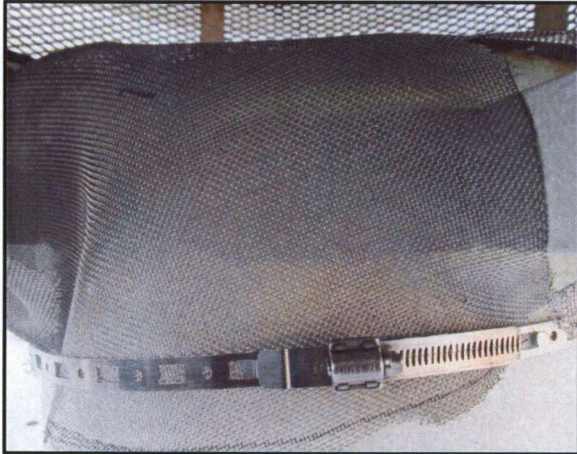

Roof vent screen

Security

- Fence Around Site: Tank is located inside a fenced-in area.
- Access Hatch Locked: Access Hatch is Secured.
- Evidence Of Vandalism: There is not evidence of vandalism.

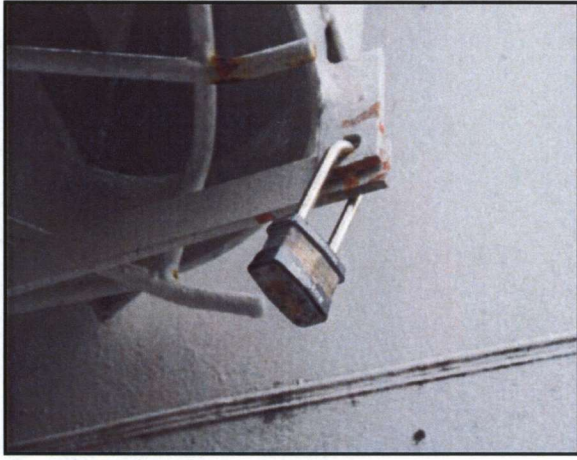


Ladder gate locked



Roof access hatch locked

Structural

- Foundation: Foundation is in good condition and there is no erosion occurring around foundation.
- Access Ladders: Dry-side access ladder styles, rungs and connections are in good condition.
- Watertight Conditions: There are no visible leaks at manway, riser or legs.
- Interior Ladders: This tank does not have an interior ladder
- Roof: Roof Trusses, Rafters and their connections are sound and in good condition.
- Vents: Roof vent is beginning to show minor corrosion and will be scheduled for repair or replacement.
- Overflow Pipe: Overflow Pipe is in good condition.
- Welds: Weld Seams are in good condition.

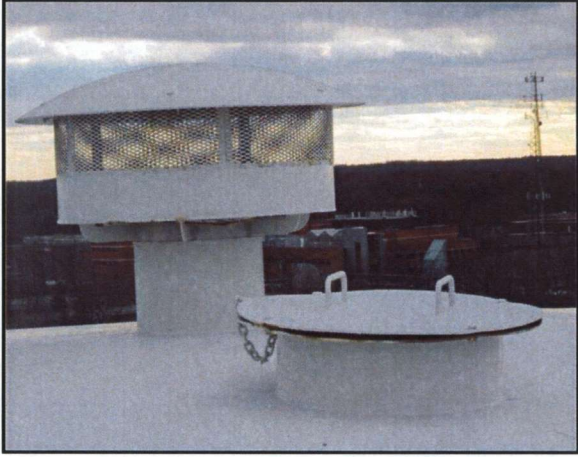

Roof vent
